

Redacted structural sample. Same report template as the production agent output. Client names, project codenames, and personnel are anonymized. One project deep dive is shown in full; remaining projects use the same section structure.



Portfolio Actuals vs Forecast — June 8, 2026

⚠️ Partial run (example): Report generated from canonical Projects DB + Open Tasks. PM meeting-note enrichment was not available in the sample window (no matching alignment notes in the past week).

Report date: June 8, 2026 · Prepared by: Notion custom agent · Portfolio: 7 projects · Active: 5 · Halted: 2 (resource crunch) · Completed: 0




Executive Summary

Project	Status	Phase	Forecasted	Actual	Variance	Tasks (Done / Total)
Project Alpha — Internal PM Tool	Delayed	Development, Deployed	Oct 6, 2025 → Mar 23, 2026	Oct 6, 2025 → Mar 20, 2026	Go-live passed; status In progress	49 / 49
Project Beta — CRM Dashboard	Sign-off pending	Testing, Deployed	Oct 6, 2025 → Mar 27, 2026	Oct 6, 2025 → Mar 20, 2026	Build complete; acceptance pending	54 / 63
Project Gamma — Community Platform	Overdue	Development	Feb 11 → May 27, 2026	Feb 11 → (open)	Bug fixes; scope pending approval	164 / 180
Project Delta — Exec Dashboard	Delayed	Planning, Development	Feb 23 → Apr 10, 2026	Feb 23 → Mar 2, 2026	High completion; closeout unclear	29 / 30
Project Epsilon — QA Hub	On hold	Maintenance only	Feb 23 → Mar 31, 2026	Feb 23 → Apr 21, 2026	Go-live passed; rebaseline needed	33 / 37
Project Zeta — Stakeholder AI	Halted	—	Feb 11 → Jul 10, 2026	Paused Mar 28, 2026	Halted — resource crunch	47 / 52
Project Eta — Document AI	Halted	—	Feb 16 → Jun 12, 2026	Paused Apr 4, 2026	Halted — resource crunch	31 / 34

Rows above mirror the live executive summary table. Project Gamma is expanded on the following pages. Projects Zeta and Eta are halted (resource crunch); 5 projects remain active.

 Portfolio Gantt — Forecasted vs Actuals

Agent renders an inline Mermaid Gantt in production. Below is the same visual structure in redacted form.

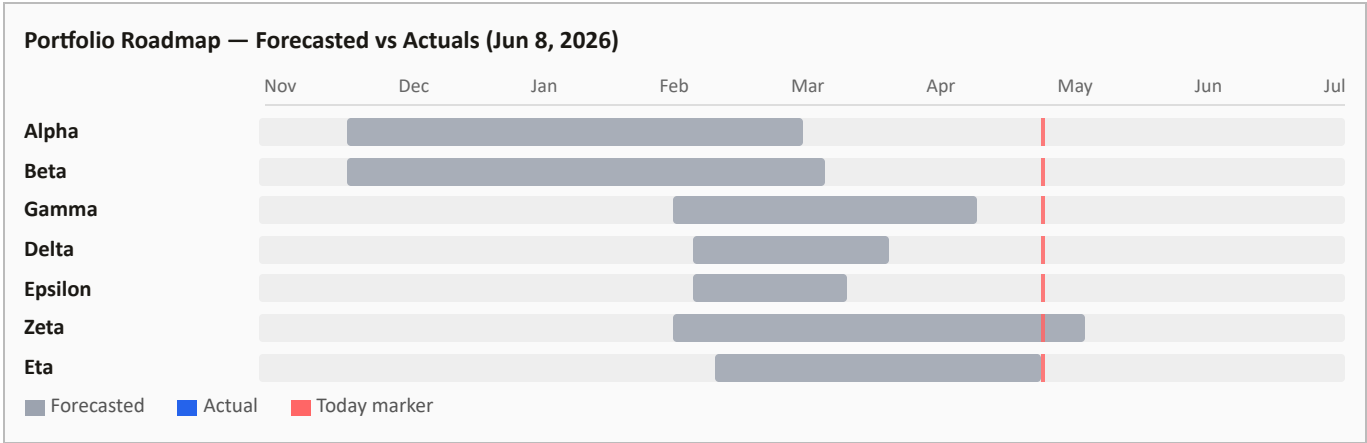


 Project Deep Dives — Milestones & Task Tie-Out

Production reports include one deep-dive section per active project. This sample shows the full template for **Project Gamma** only. Projects Alpha, Beta, Delta, and Epsilon follow the same structure. Zeta and Eta are halted.

📁 3. Project Gamma — Community Platform — Overdue

Builder: [Redacted] · Start date: Feb 11, 2026 · Go-live: May 27, 2026 · Priority: High · Task completion: 91% (164/180)

Milestone	Forecasted	Actual	Variance	Status
Go-live (Projects DB)	May 27, 2026	—	Past due	Status still In progress
Readiness tie-out	—	—	In flight	Bug fixes underway; new requests pending executive approval

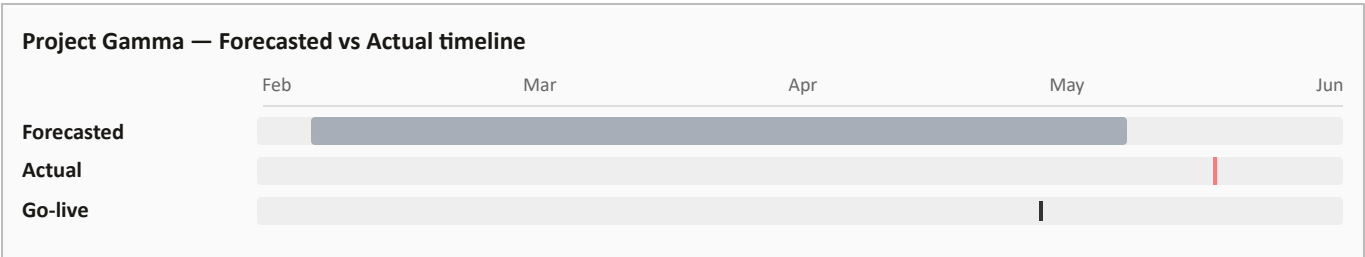

📊 Task Analysis: 164 completed · 2 in progress · 5 pending · 4 under review · 5 archived (180 total)

- **Completion rate:** 91%
- **Overdue tasks:** none in open-task set
- **Upcoming this week:** grouped by theme below

Open task detail (anonymized examples):

- **Production bug fixes (in progress):** API auth error on file upload · badge count mismatch under review
- **Go-live support (in progress / pending):** telephony warmup · deployment reset strategy for production cutover
- **Architecture review (under review):** permissions model · audit log design
- **Approval-dependent scope (pending executive sign-off):** catalog expansion · role mapping update

⚠️ **Risks:** Separate launch-blocking bug fixes from scope awaiting executive approval. Track approvals on a different line than active engineering work.

● Top Portfolio Risks

Risk	Project	Impact	Severity
Go-live passed while status still In progress	Alpha, Gamma, Delta	Hard to interpret variance and true closure state	High
Approval-dependent scope mixed with active bug fixes	Gamma	Execution split across two workstreams	High
Go-live within 7 days with open gating tasks	Eta	Release risk if UAT items block go/no-go	Medium

▶▶ This Week — Key Actions (Jun 8–14)

Project	Key action	Owner
Gamma	Close active bug-fix queue; track executive approvals separately for new requests	[Engineering lead], [Executive stakeholders]
Alpha	Confirm closeout semantics; align go-live with project status	[PM owner]
Eta	Go/no-go tie-out before release; confirm open tasks against UAT gates	[Tech lead]

✦ Data Sources Used

- **Projects DB** — status, phase, start date, go-live, owner, linked tasks
- **Open Tasks DB** — counts by status (completed, in progress, pending, under review, archived)
- **Meeting notes** — PM alignment cadence (when matched in query window)
- **Reference reports** — format/structure only (not used as live data)

⚠ Data Quality Issues (sample)

- Stale go-live vs status mismatch on multiple projects (go-live in the past, status still In progress)
- Approval-dependent scope should be tracked separately from launch-blocking fixes (Project Gamma)
- Meeting-note enrichment unavailable in partial run window

🔄 Key Changes Since Last Report (sample)

- Projects Zeta and Eta: halted due to resource crunch — active portfolio count now 5 of 7
- Project Gamma: go-live date corrected in Projects DB — confirm whether rebaseline or data fix

How the agent produces this report

Step	What happens
1. Trigger	Scheduled every Monday at 8:00 AM (or manual run in Notion)
2. Data pull	Reads canonical Projects + Open Tasks databases; optional meeting-note enrichment
3. Format rules	Uses prior reports for layout/Gantt style only — not for metrics
4. Output	Writes executive summary, portfolio Gantt, per-project deep dives, risks, and action items to Portfolio Status Report page

Redacted structural sample for portfolio use. Anonymized names; metrics and section order reflect a production Notion custom agent workflow at Aosenuma.ai (co-op).
