



Portfolio Actuals vs Forecast — June 8, 2026

⚠️ Partial run: This report was generated from canonical **Projects DB + Open Tasks**. Recent PM alignment meeting-note enrichment was not available (no matching AI meeting notes in the past week).

Report Date: June 8, 2026 · **Prepared by:** Notion AI · **Portfolio:** 7 projects · **Active:** 6 · **Completed:** 1 · **Not Started:** 0

Executive Summary

Project	Status	Phase	Forecasted	Actual	Variance	Tasks (Done / Total)
 AI PMO Tool	Delayed (Parking lot)	Development, Deployed, Development of v2	Oct 6, 2025 → Mar 23, 2026	Oct 6, 2025 → Mar 20, 2026	🔴 Go Live passed (Mar 23) while Estado is still In progress — confirm whether post-handover tail should have a new Go Live or Estado should move to Completed	49 / 49
 AI CRM Dashboard	Final sign-off pending	Development, Testing, Development of v2, Deployed	Oct 6, 2025 → Mar 27, 2026	Oct 6, 2025 → Mar 20, 2026	🟡 Build complete; final sign-off pending	54 / 63
 Woodside Community Management system	On Track	Development	Feb 11, 2026 → May 27, 2026	Feb 11, 2026 → <i>(open)</i>	🟡 Bug fixes are underway; remaining new requests are pending approval from Jorge and Daniel	164 / 180
 AIVI-AICRM-AIPMO (Unified Executive Dashboard)	Delayed (Parking lot)	Planning, Development, Deployed	Feb 23, 2026 → Apr 10, 2026	Feb 23, 2026 → Mar 2, 2026	🟢 Task completion is high, but Go Live is past due while Estado remains In progress —	29 / 30

Project	Status	Phase	Forecasted	Actual	Variance	Tasks (Done / Total)
					verify closure or remaining acceptance criteria	
 QA Hub	Overdue	Development of v2	Feb 23, 2026 → Mar 31, 2026	Feb 23, 2026 → Apr 21, 2026	 Go Live passed (Mar 31) while Estado is still In progress; Start Date end is after Go Live — reconcile rebaseline vs closeout	33 / 37
 STAKE AI	On Track	Development	Feb 11, 2026 → Jul 10, 2026	Feb 11, 2026 → Apr 25, 2026	 32 days remaining to Go Live	47 / 52
 RapdAI	At Risk	Testing	Feb 16, 2026 → Jun 12, 2026	Feb 16, 2026 → <i>(open)</i>	 Go Live in 4 days with 3 non-complete tasks remaining	31 / 34

 Portfolio Gantt — Forecasted vs Actuals

```
%%{init: {'theme': 'base', 'background': '#ffffff', 'themeVariables': {'taskTextColor': '#000000', 'taskTextDarkColor': '#ffffff', 'taskTextOutsideColor': '#000000', 'doneTaskBkgColor': '#6b7280', 'doneTaskBorderColor': '#4b5563', 'activeTaskBkgColor': '#2563eb', 'activeTaskBorderColor': '#1d4ed8', 'taskBkgColor': '#e5e5e5', 'taskBorderColor': '#bbbbbb', 'sectionBkgColor': '#ffffff', 'sectionBkgColor2': '#ffffff', 'gridColor': '#dddddd', 'todayLineColor': '#ff6666', 'mainBkg': '#ffffff', 'textColor': '#000000'}}}%%
gantt
    title Portfolio Roadmap – Forecasted vs Actuals (Jun 8, 2026)
    dateFormat YYYY-MM-DD
    axisFormat %b %d
    todayMarker stroke-width:2px,stroke:#f66,opacity:0.8

    section AI PMO Tool (Overdue)
    Forecasted      :crit, pmo-f, 2025-10-06, 2026-03-23
    Actual          :crit, pmo-a, 2025-10-06, 2026-06-08


    section AI CRM Dashboard (Completed)
    Forecasted      :done, crm-f, 2025-10-06, 2026-03-27
    Actual          :active, crm-a, 2025-10-06, 2026-06-08

    section Woodside (Overdue)
    Forecasted      :crit, ws-f, 2026-02-11, 2026-05-27
    Actual          :crit, ws-a, 2026-02-11, 2026-06-08

    section Unified Exec Dashboard (Overdue)
    Forecasted      :crit, ued-f, 2026-02-23, 2026-04-10
    Actual          :crit, ued-a, 2026-02-23, 2026-06-08

    section QA Hub (Overdue)
    Forecasted      :crit, qa-f, 2026-02-23, 2026-03-31
    Actual          :crit, qa-a, 2026-02-23, 2026-04-21

    section STAKE AI (On Track)
    Forecasted      :active, sa-f, 2026-02-11, 2026-07-10
```

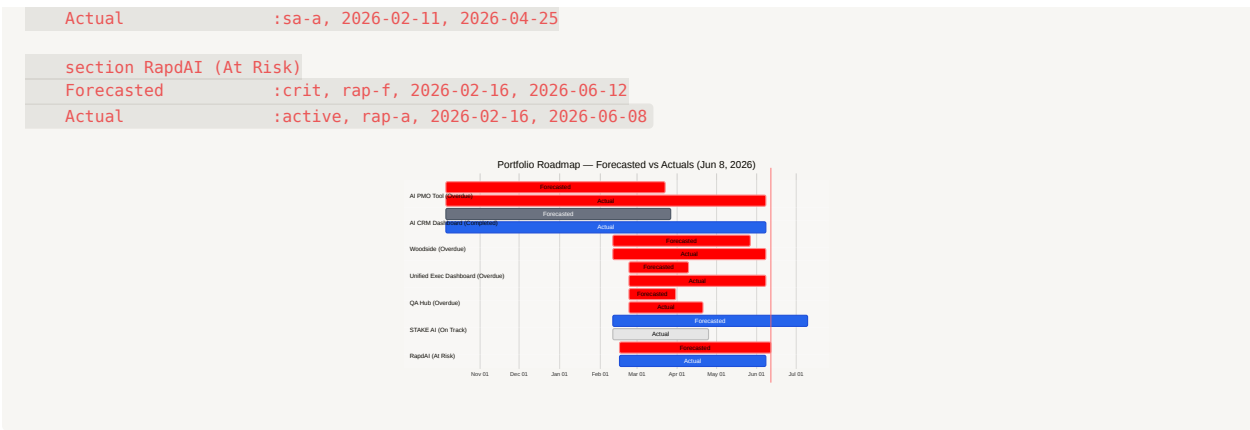

📦 Project Deep Dives — Milestones & Task Tie-Out

🔧 1. AI PMO Tool — Delayed (Parking lot)

Builder: Vaishnavi · **Start Date:** Oct 6, 2025 · **Go Live:** Mar 23, 2026 · **Priority:** Media · **Task Completion:** 100% (49/49)

Milestone	Forecasted	Actual	Variance	Status
Project start	Oct 6, 2025	Oct 6, 2025	🟢 0d	✅ Done
Execution end (Start Date end)	—	Mar 20, 2026	🟢	✅ Done
Go Live (Projects DB)	Mar 23, 2026	Mar 23, 2026	🟡 Verify semantics	⚠️ Estado still In progress
Post-handover tail closeout	—	—	—	⚠️ Confirm if any “tail” work exists outside Open Tasks
Estado hygiene	—	—	—	⚠️ Align Estado with reality





Task Analysis: 49 completed · 0 in progress · 0 pending **(49 total)**
Completion rate: 100%
Overdue tasks: none.
Upcoming this week: none.



Risks: “Go Live” is in the past while Estado remains In progress — reporting confusion risk.

✓ **2. AI CRM Dashboard — Final sign-off pending**

Builder: Israel, Madhura, Aneth · **Start Date:** Oct 6, 2025 · **Go Live:** Mar 27, 2026 · **Priority:** Media · **Task Completion:** 86% (54/63)

Milestone	Forecasted	Actual	Variance	Status
Project start	Oct 6, 2025	Oct 6, 2025	0d	✓ Done
Execution end (Start Date end)	—	Mar 20, 2026		✓ Done
Go Live	Mar 27, 2026	Mar 27, 2026		✓ Done
Archived tail	—	—	—	✓ Archived (9)
Metrics validation follow-up	—	—	—	⚠ Optional

```
%%{init: {'theme': 'base', 'background': '#ffffff', 'themeVariables': {'taskTextColor': '#000000', 'taskTextDarkColor': '#ffffff', 'taskTextOutsideColor': '#000000', 'doneTaskBkgColor': '#6b7280', 'doneTaskBorderColor': '#4b5563', 'activeTaskBkgColor': '#2563eb', 'activeTaskBorderColor': '#1d4ed8', 'taskBkgColor': '#e5e5e5', 'taskBorderColor': '#bbbbbb', 'sectionBkgColor': '#ffffff', 'sectionBkgColor2': '#ffffff', 'gridColor': '#dddddd', 'todayLineColor': '#ff6666', 'mainBkg': '#ffffff', 'textColor': '#000000'}}}%  
gantt  
  title AI CRM Dashboard  
  dateFormat YYYY-MM-DD  
  axisFormat %b %d  
  
  section Forecasted  
  Forecasted (Start → Go Live) :done, f1, 2025-10-06, 2026-03-27  
  
  section Actual  
  Actual (Start → End) :active, a1, 2025-10-06, 2026-06-08
```



Task Analysis: 54 completed · 0 in progress · 0 pending · 9 archived **(63 total)**
Completion rate: 86%
Overdue tasks: none.
Upcoming this week: none.



Risks: Ensure archived tail work is truly non-blocking (optional hygiene).

3. Woodside Community Management system — Overdue

Start Date: Feb 11, 2026 · **Go Live:** May 27, 2026 · **Priority:** Alta · **Task Completion:** 91% (164/180)

Milestone	Forecasted	Actual	Variance	Status
Go Live (Projects DB)	May 27, 2026	—	 Past due	 Estado still In progress
Readiness tie-out	—	—		Bug fixes underway; remaining new requests pending approval from Jorge and Daniel



Task Analysis: 164 completed · 2 in progress · 5 pending · 4 under review · 5 archived **(180 total)**

Completion rate: 91%

Upcoming / open Woodside task detail:

- **Bug fixes underway:** File upload returns 401 Unauthorized — In Progress, owner Lochan Enugula, due May 26; badge count mismatch — Under Review, owner Fengqi Hu, due May 26.
- **Bug fixes pending:** Reply to citizen button not working — Pending, owner Lochan Enugula, due May 22; Agent cannot view assigned cases in Dashboard — Pending, owner Manan Patel, due Jun 5; Chatbot reset/restart issue — Pending, owner José María Esquivel Muñoz, due Jun 5; Chatbot conversation close/end option — Pending, owner José María Esquivel Muñoz, due Jun 5.
- **Readiness / go-live support:** Phone Line Warmup — In Progress, owner José María Esquivel Muñoz, due May 28; Research Zeabur clone and database reset strategy for production Go-Live — Pending, owner Manan Patel, due Jun 2.
- **Architecture / review items:** Permissions & Audit Log architecture review — Under Review, owner José María Esquivel Muñoz, due May 22; State Machine / SLA / Permissions / Audit Log architecture review — Under Review, owner José María Esquivel Muñoz, due May 22.
- **New requests pending approval:** Expand Municipality Catalog for Woodside MAC operational scope — Under Review, owner Lochan Enugula, due Jun 3; Update Woodside MAC Departments to match framework roles & responsibilities — Pending, owner Niharika Asopa, due Jun 10. These approval-dependent items are pending Jorge and Daniel.



Risks: Bug fixes are underway; remaining new requests are pending approval from Jorge and Daniel. Track approvals separately from launch-blocking fixes.

4. Unified Executive Dashboard — Delayed (Parking lot)

Builder: Krisha Lakhani, Kalai Arun, Aneth, Vaishnavi, Madhura Adadande · **Start Date:** Feb 23, 2026 · **Go Live:** Apr 10, 2026 · **Priority:** Media · **Task Completion:** 97% (29/30)

Milestone	Forecasted	Actual	Variance	Status
Project start	Feb 23, 2026	Feb 23, 2026	 0d	 Done
Execution end (Start Date end)	—	Mar 2, 2026		 Done
Go Live (Projects DB)	Apr 10, 2026	—	 Go Live passed	 Verify closeout

Milestone	Forecasted	Actual	Variance	Status
Remaining open task(s)	—	—	—	⚠️ 1 task non-complete
Decision: keep separate from AI CRM	—	—	—	🔗 Continue reporting separately

```

%%{init: {'theme': 'base', 'background': '#ffffff', 'themeVariables': {'taskTextColor': '#000000', 'taskTextDarkColor': '#ffffff', 'taskTextOutsideColor': '#000000', 'doneTaskBkgColor': '#6b7280', 'doneTaskBorderColor': '#4b5563', 'activeTaskBkgColor': '#2563eb', 'activeTaskBorderColor': '#1d4ed8', 'taskBkgColor': '#e5e5e5', 'taskBorderColor': '#bbbbbb', 'sectionBkgColor': '#ffffff', 'sectionBkgColor2': '#ffffff', 'gridColor': '#dddddd', 'todayLineColor': '#ff6666', 'mainBkg': '#ffffff', 'textColor': '#000000'}}}%

```

gantt

title Unified Executive Dashboard

dateFormat YYYY-MM-DD

axisFormat %b %d

section Forecasted

Forecasted (Start → Go Live) :crit, f1, 2026-02-23, 2026-05-25

section Actual

Actual (Start → End) :crit, a1, 2026-02-23, 2026-06-08



Task Analysis: 29 completed · 1 in progress **(30 total)**

Completion rate: 97%

Overdue tasks: none found in the relation set.

Upcoming this week: none found.



Risks: Go Live passed but Estado still In progress — closure ambiguity.



5. QA Hub — On Hold (Maintenance only)

Builder: Lalit Jadhav, Vraj Patel, Carlos Hernandez · **Start Date:** Feb 23, 2026 · **Go Live:** TBD · **Priority:** Alta ·

Task Completion: 89% (33/37)

Milestone	Forecasted	Actual	Variance	Status
Program kickoff (Start Date)	Feb 23, 2026	Feb 23, 2026	● 0d	✅ Done
Go Live (Projects DB)	TBD	—	⏸ On hold since May 11 (maintenance only)	⏸ On Hold
Start Date end (Projects DB)	—	Apr 21, 2026	● Indicates work continued beyond Go Live	⚠️ Reconcile dates
Overdue task list	—	—	—	⚠️ Not computed in this run
Champion / governance updates	—	—	—	⚠️ Not updated in this run

```

%%{init: {'theme': 'base', 'background': '#ffffff', 'themeVariables': {'taskTextColor': '#000000', 'taskTextDarkColor': '#000000', 'taskTextOutsideColor': '#000000', 'doneTaskBkgColor': '#6b7280', 'doneTaskBorderColor': '#4b5563', 'activeTaskBkgColor': '#2563eb', 'activeTaskBorderColor': '#1d4ed8', 'taskBkgColor': '#e5e5e5', 'taskBorderColor': '#bbbbbb', 'sectionBkgColor': '#ffffff', 'sectionBkgColor2': '#ffffff', 'gridColor': '#d4d4d4', 'todayLineColor': '#ff6666', 'mainBkg': '#ffffff', 'textColor': '#000000'}}}%

```

gantt

```

title QA Hub
dateFormat YYYY-MM-DD
axisFormat %b %d


```

section Forecasted

Forecasted (Start → Go Live) :crit, f1, 2026-02-23, 2026-03-31

section Actual

Actual (Start → End) :crit, a1, 2026-02-23, 2026-04-21



Task Analysis: 33 completed · 2 in progress · 1 pending · 1 archived (**37 total**)

Completion rate: 89%

Overdue tasks / Upcoming this week: Not computed in this partial run.



Hold reason: Dev capacity reassigned to STAKE AI, Woodside, RapdAI + LLM Observability/QA (since May 11).

Scope: Maintenance only (critical fixes). No v2 feature work.

Plan: Rebaseline Go Live once capacity frees.



6. STAKE AI — On Track

Builder: Abhijeet Deshpande, Naman Jindal (+ team) · **Start Date:** Feb 11, 2026 · **Go Live:** Jul 10, 2026 ·

Priority: Alta · **Task Completion:** 90% (47/52)

Milestone	Forecasted	Actual	Variance	Status
Go Live	Jul 10, 2026	—	● 32 days remaining	⌚ Upcoming
Stake AI- Elawan	Jul 8. 2026			Today



Task Analysis: 47 completed · 3 in progress · 0 pending · 1 under review · 1 archived (**52 total**)

Danitz beta onboarding (May 28–Jun 5):

- Onboarding enablement is complete (*credentials + manual acknowledged*)
- No structured findings logged yet via the formal bug form
- Follow-up meeting is the primary intake for findings/challenges
- Near-term risk: **feedback latency / unstructured intake** → delays P0/P1 triage
- Meeting is due today

Completion rate: 90%



Risks: Actual date range is closed (ends Apr 25) but Estado remains In progress — clarify whether Start Date end represents a phase vs full project timeline.

⚡ 7. RapdAI — At Risk

Builder: Abhijeet, Naman, Carlos · **Start Date:** Feb 16, 2026 · **Go Live:** Jun 12, 2026 · **Priority:** Media · **Task Completion:** 91% (31/34)

Milestone	Forecasted	Actual	Variance	Status
Beta UAT window (Projects DB)	May 11–Jun 5, 2026	—	—	In progress
Go Live	Jun 12, 2026	—	4 days remaining	Upcoming
Legal Analysis Architecture	Jul 8, 2026	—	—	In progress
Integration Plan	Jul 8, 2026	—	—	In progress



Task Analysis: 31 completed · 1 in progress · 2 pending **(34 total)**

- Legal Analysis architecture is formed
- Integration Plan is formed

Completion rate: 91%



Risks: Go Live is within a week; verify whether the remaining 3 non-complete items include any Go/No-Go gates (auth, processing performance, reporting, analytics, isolation, docs/training).

🔴 Top Portfolio Risks

Risk	Project	Impact	Severity
Go Live passed while Estado is still In progress (status/date semantics mismatch)	AI PMO Tool	Reporting ambiguity; hard to interpret variance and true closure state	High
Bug fixes underway; remaining new requests pending approval	Woodside	Execution risk is now split between active bug-fix completion and Jorge/Daniel approval for new requests	High
Go Live passed while Estado is still In progress	Unified Exec Dashboard	Unclear acceptance criteria remaining; difficult to assess true project health	High
Go Live is in the past + Start Date end after Go Live	QA Hub	Timeline semantics unclear; remaining work may be untracked or not reflected	Medium
Go Live in 4 days with 3 non-complete tasks	RapdAI	Schedule risk if remaining items are gating	Medium

🔁 This Week — Key Actions (Jun 8–14)

Project	Key Action	Owner
AI PMO Tool	Confirm whether the project is truly complete; align Estado + Go Live semantics (closeout vs post-handover tail)	Pooja Bernice
Woodside	Continue active bug fixes (file upload 401, badge count mismatch, reply button, dashboard assignment visibility, chatbot reset/close flow); complete go-live support tasks (phone line warmup, Zeabur clone/database reset strategy); secure Jorge and Daniel approval for remaining new requests (municipality catalog expansion + department-role updates)	Jorge, Daniel, Lochan, Fengqi, Manan, José María, Niharika
Unified Exec Dashboard	Confirm acceptance criteria; close the remaining non-complete task or re-baseline Go Live/Estado	Krishna Lakhani, Kalai Arun
QA Hub	Reconcile Mar 31 Go Live vs Apr 21 Start Date end; explicitly mark maintenance-only vs active execution and set a new Go Live if needed	Lalit Jadhav
RapdAI	Go/No-Go tie-out for Jun 12: confirm remaining 3 tasks + UAT outcomes covering items (performance, reports, analytics, docs/training)	Abhijeet Deshpande, Naman Jindal



Data Sources Used

- **Projects** — Estado, Project Phase, Start Date, Go Live, Builder, Tasks relation
- **Tasks** (Open Tasks) — task counts by status (Completed / In Progress / Pending / Under Review / Archived)



Data Quality Issues

- **Stale Go Live vs Estado mismatch:** AI PMO Tool (Go Live Mar 23), Woodside (Go Live May 27), Unified Exec Dashboard (Go Live Apr 10), QA Hub (Go Live Mar 31) are all past due while Estado remains In progress.
- **Woodside:** Bug fixes are underway; remaining new requests are pending approval from Jorge and Daniel, so approval-dependent scope should be tracked separately from active bug-fix work.
- **QA Hub:** Start Date end (Apr 21) is after Go Live (Mar 31) — clarify whether Go Live should be rebaselined, or if Go Live represents a sub-scope.
- **Meeting-note enrichment:** No AI meeting notes matched the “PM/alignment/readiness” query in the past week window.



Key Changes Since Last Report (June 1, 2026)

- Woodside: Go Live now shows **May 27** (previous report showed Jun 5 / earlier rebaseline) — confirm whether this is a correction or a missed date.
- RapdAI: Now 31/34 completed (previously 30/34).
